



VB TRAIL UPDATE




Steve Lambert | 09/09/2026




CITY OF VIRGINIA BEACH
**Parks &
Recreation**


Regional Trails Update

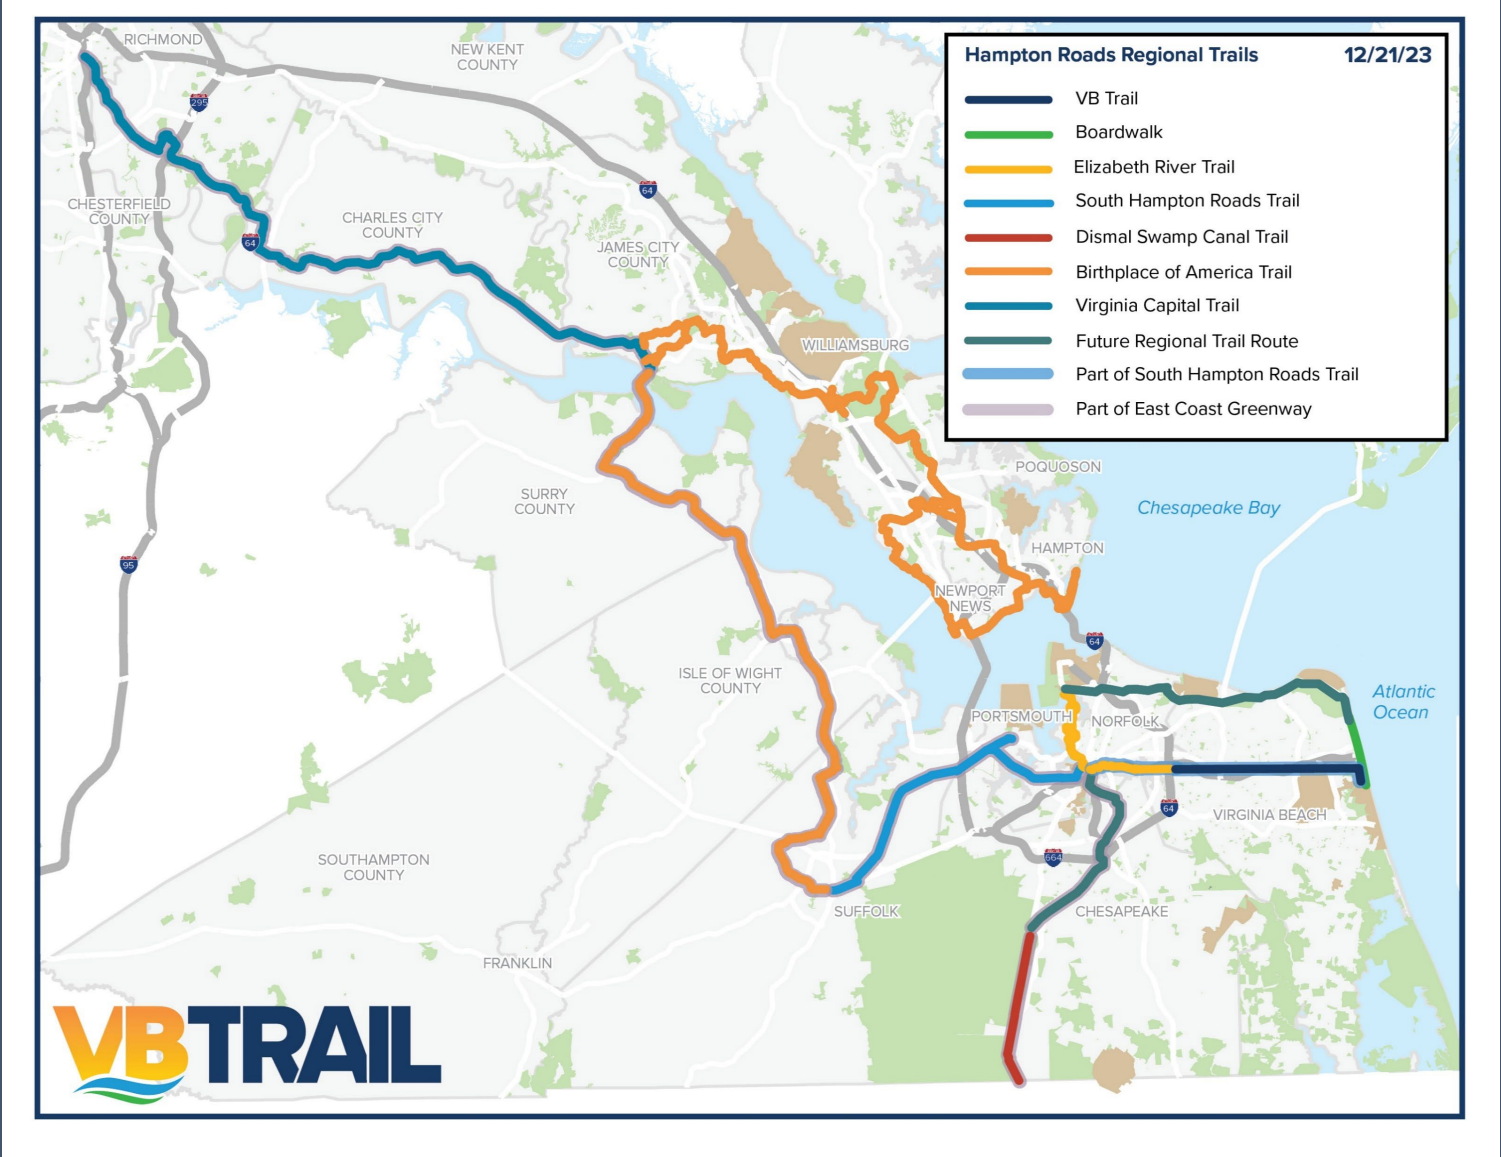

Trail757

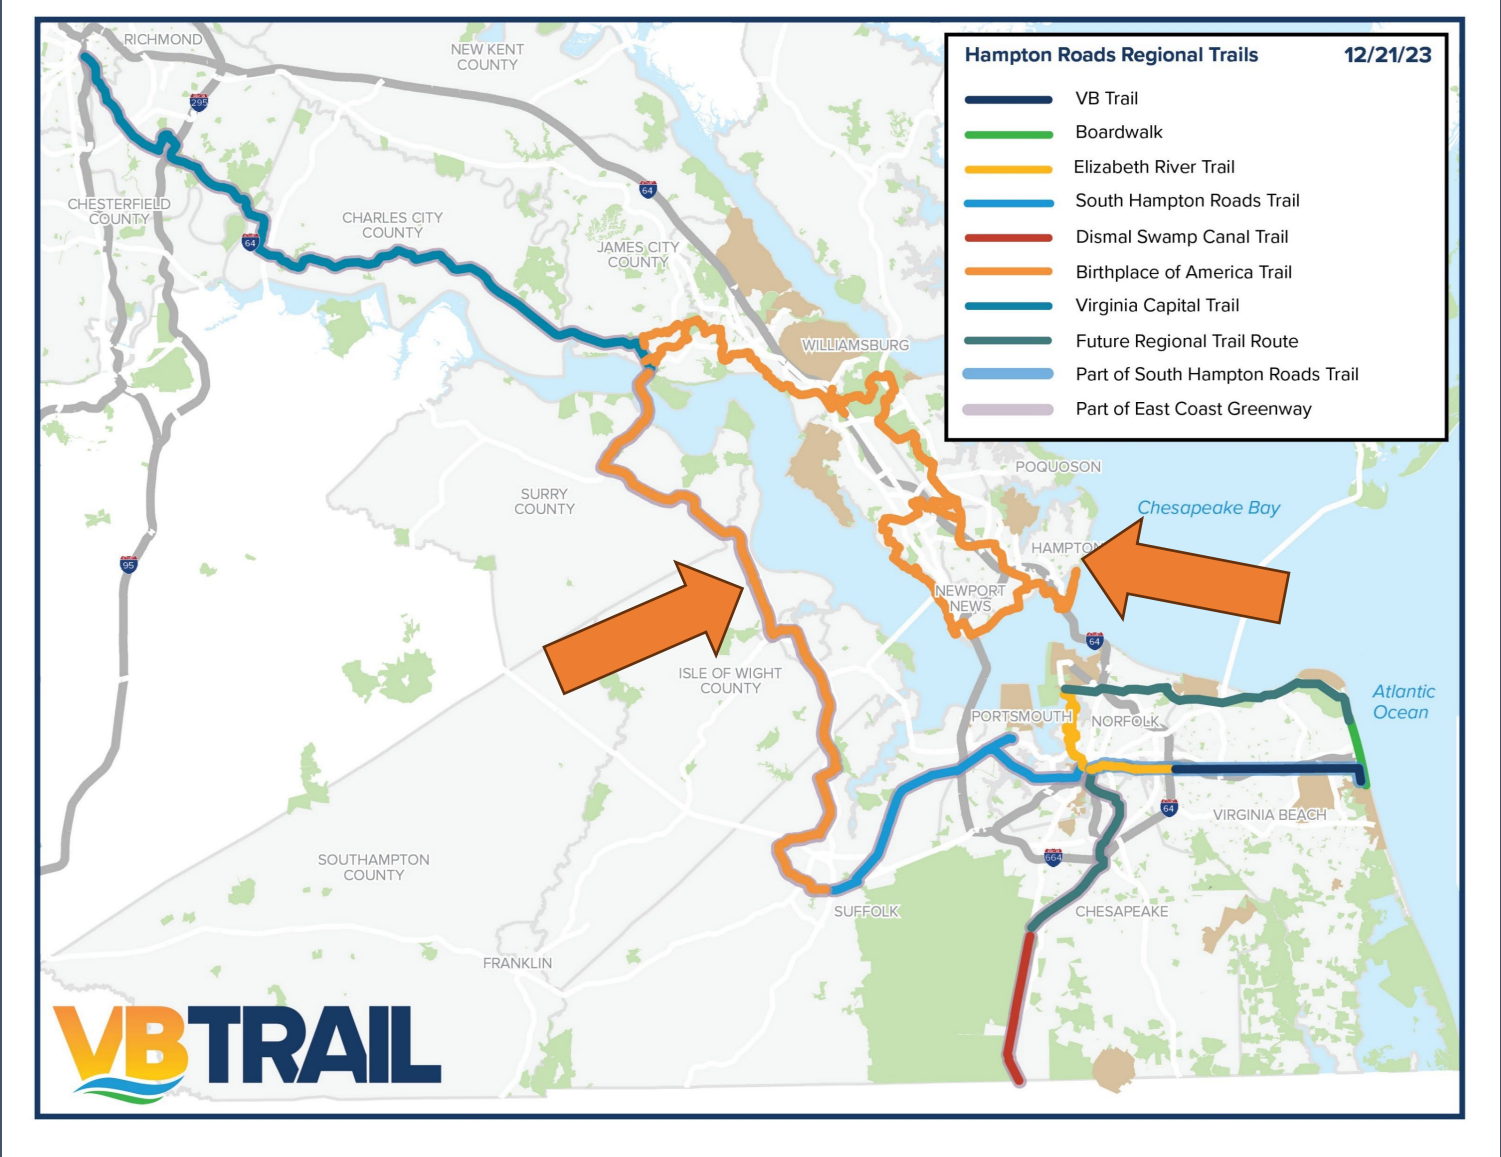

South Hampton Roads Trail

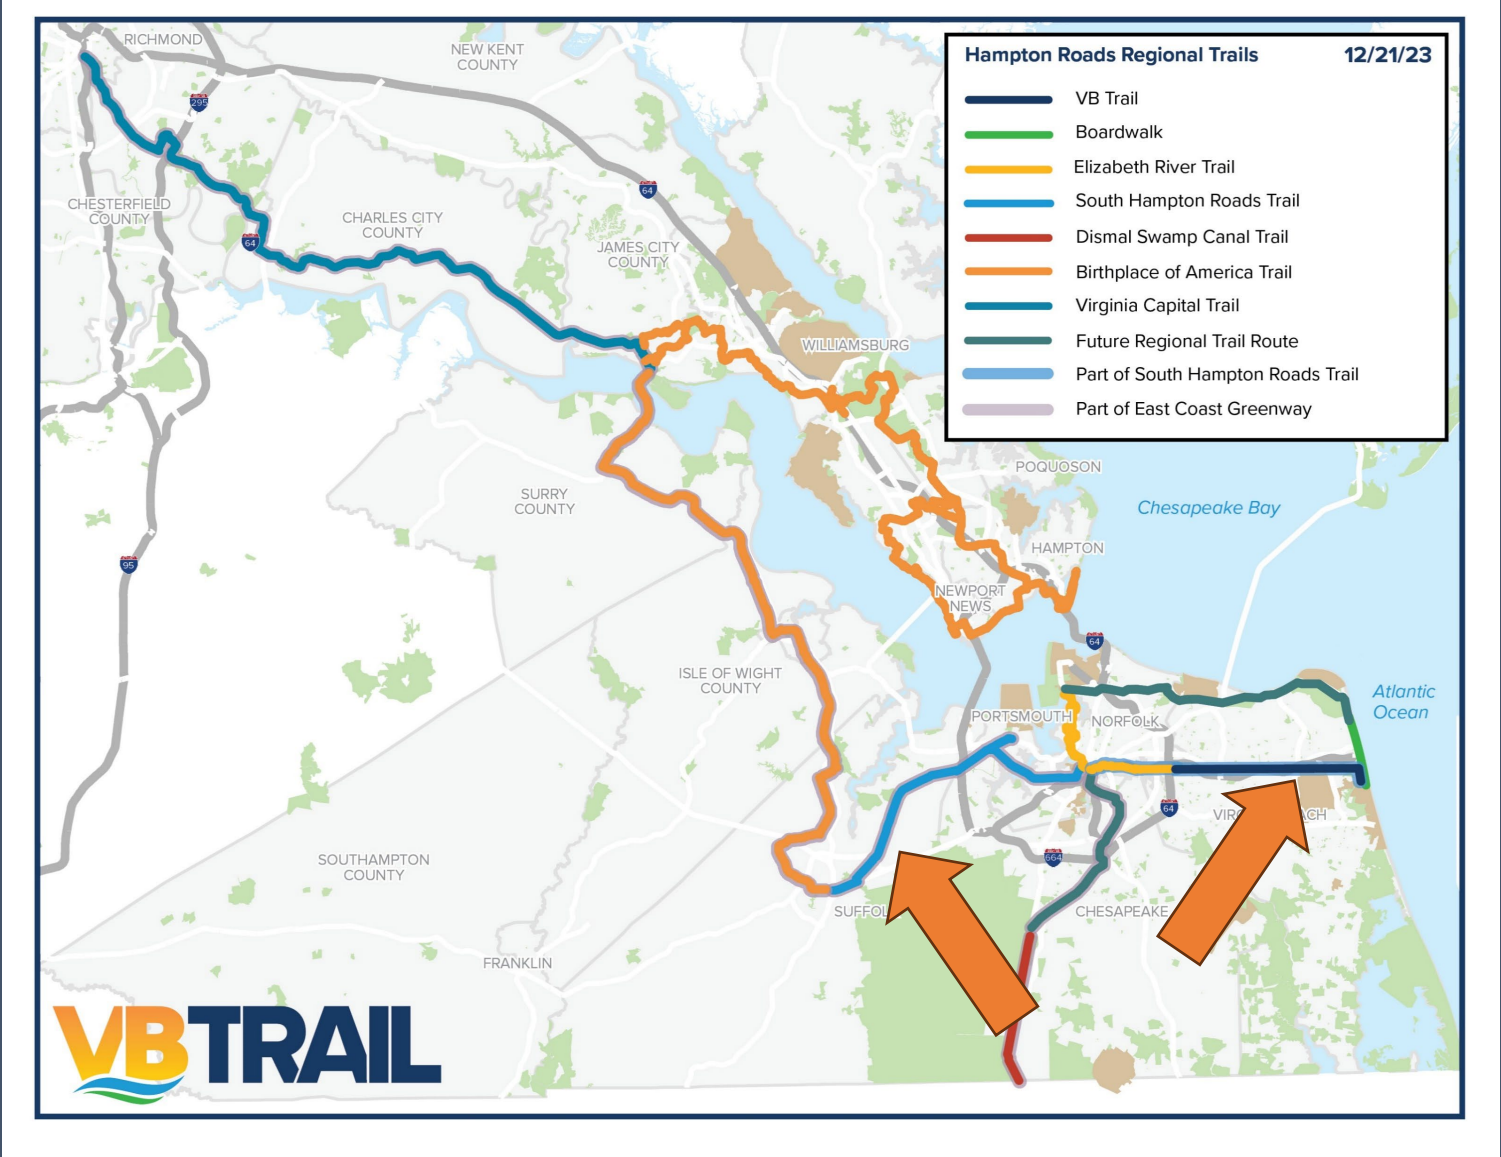

VB TRAIL

SPANNING THE CITY




Newtown Transit Hub




Town Center



Rudee Park




1981 Virginia Beach Bikeways Plan

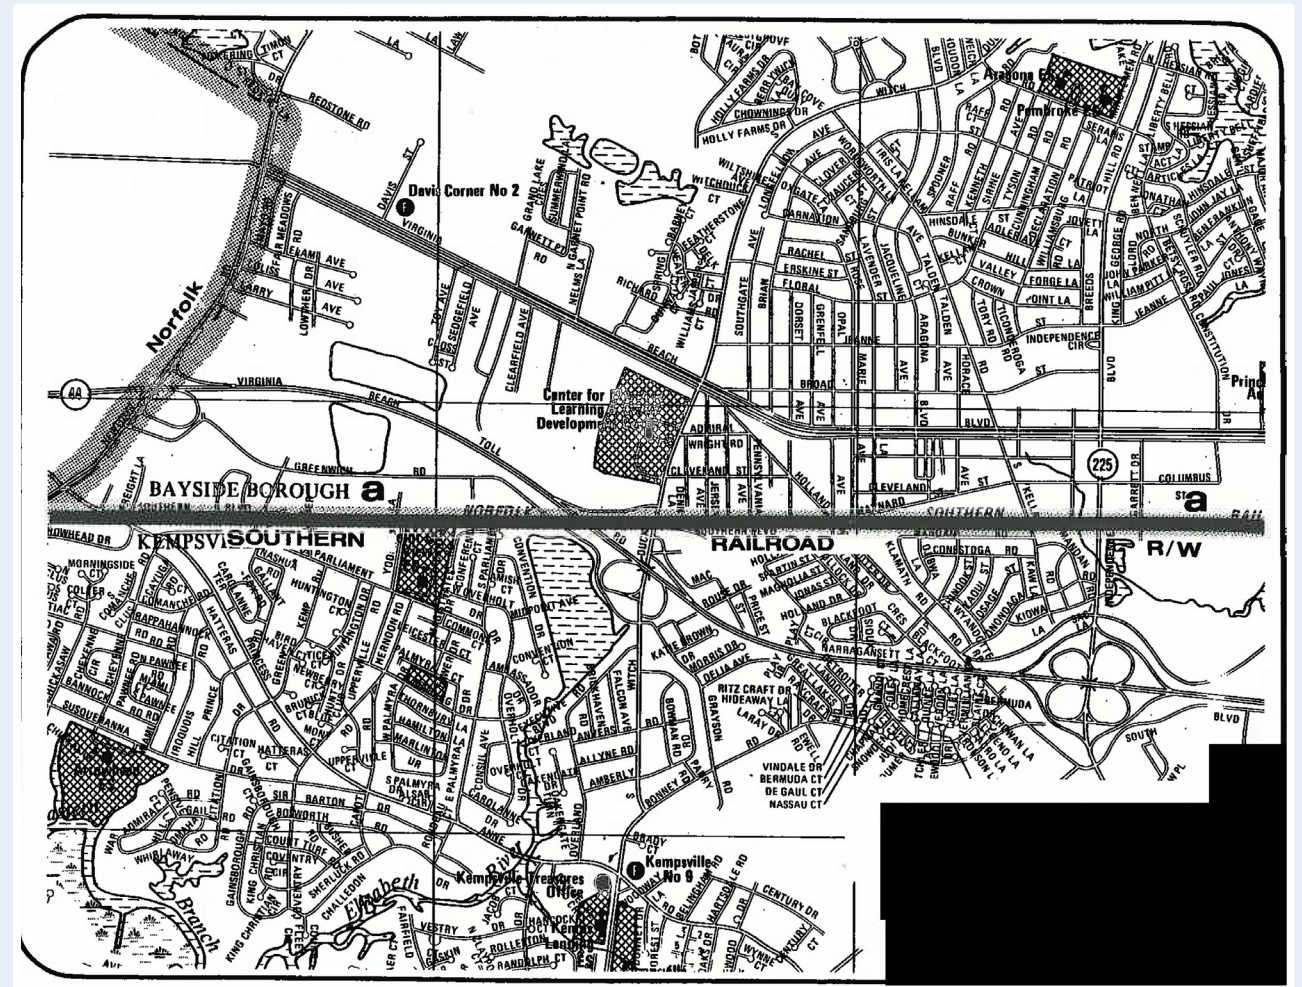


Southern Railroad ROW

VBTRAIL History

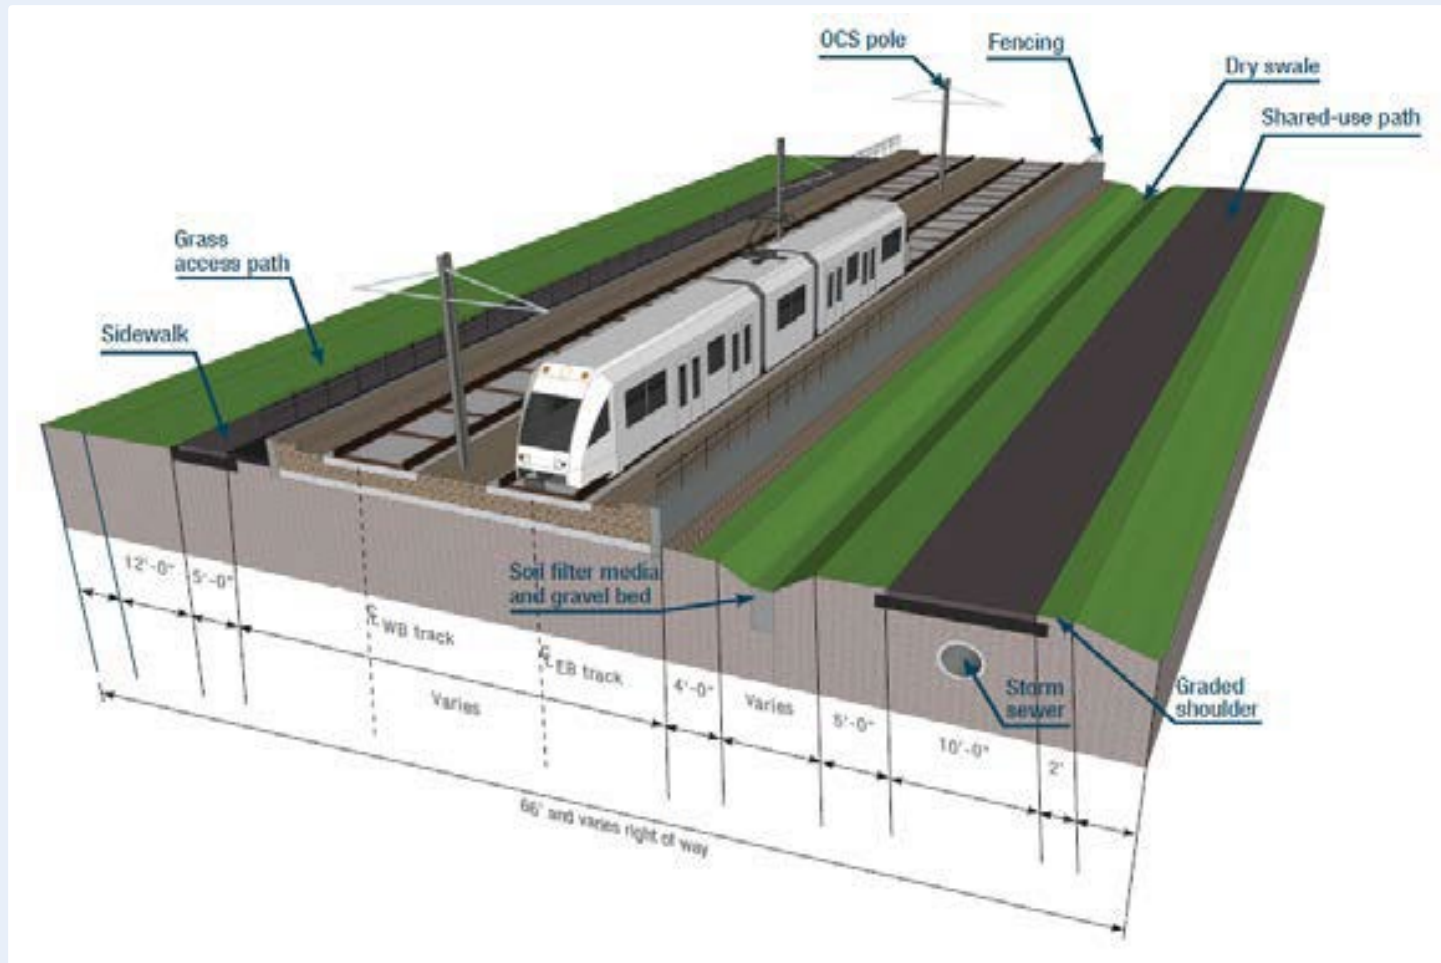

2015 Light Rail with Trail Concept Design


VBTRAIL History

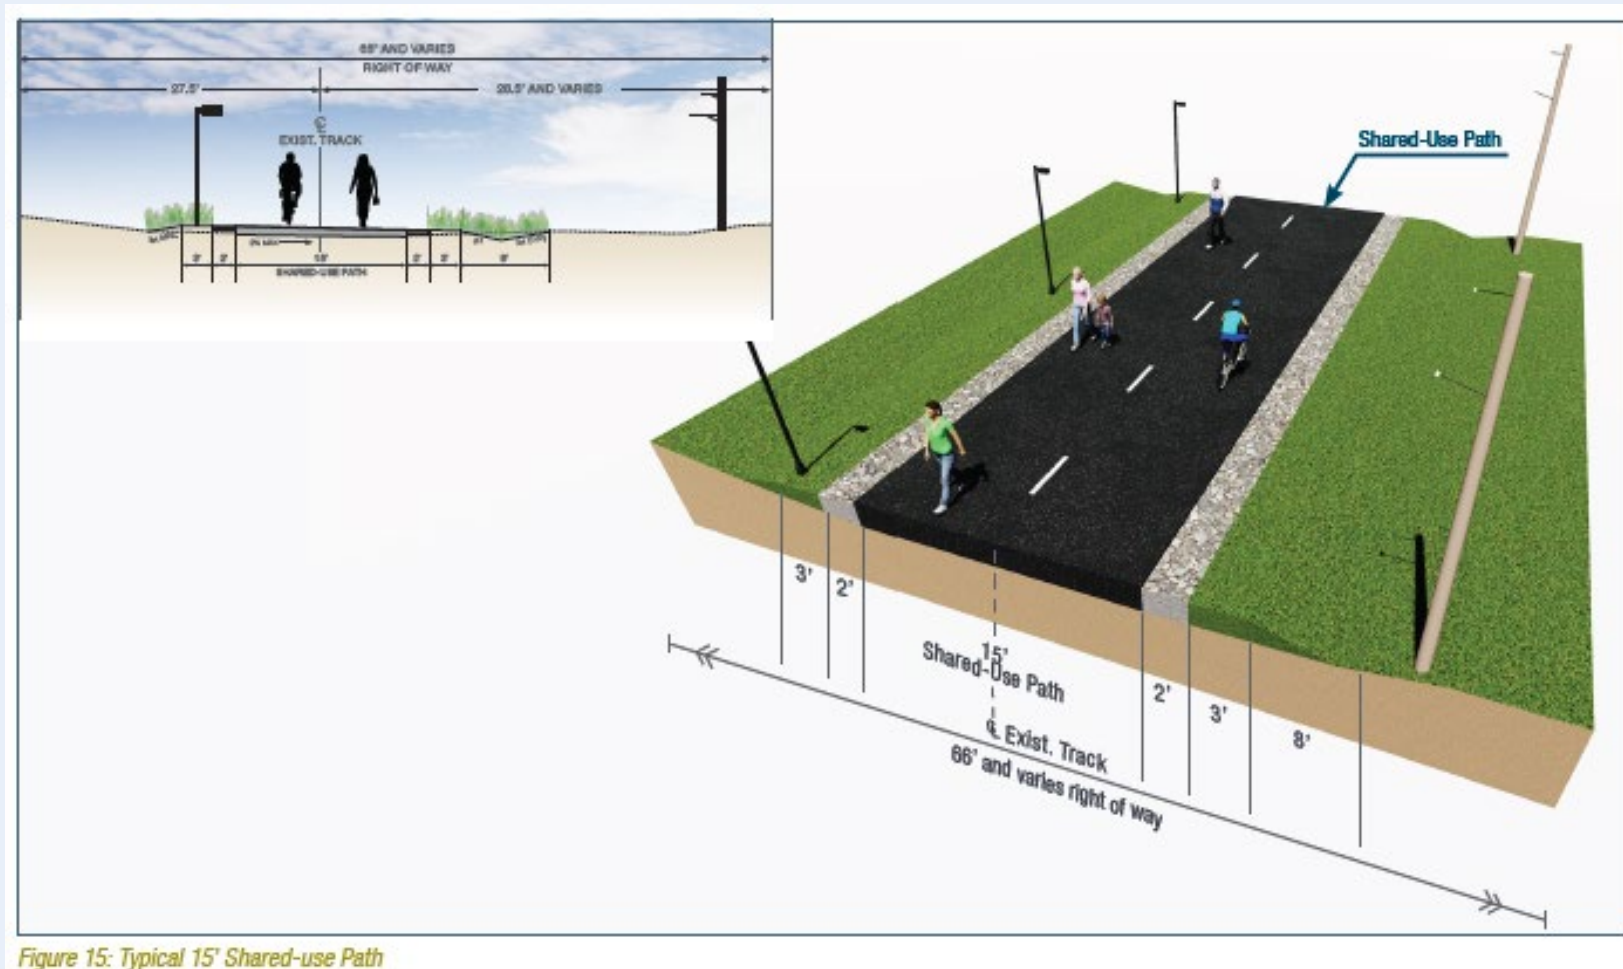

2018 NSRR Shared-Use Path Concept Study

VBTRAIL Today

- 12.6 miles Total
- 2 miles of existing trails including:
 - Recently upgraded Pacific Avenue Boardwalk
 - Winston Salem Avenue Improvement Project
 - Rudee Park
- 6 miles funded
- 4.6 miles planned

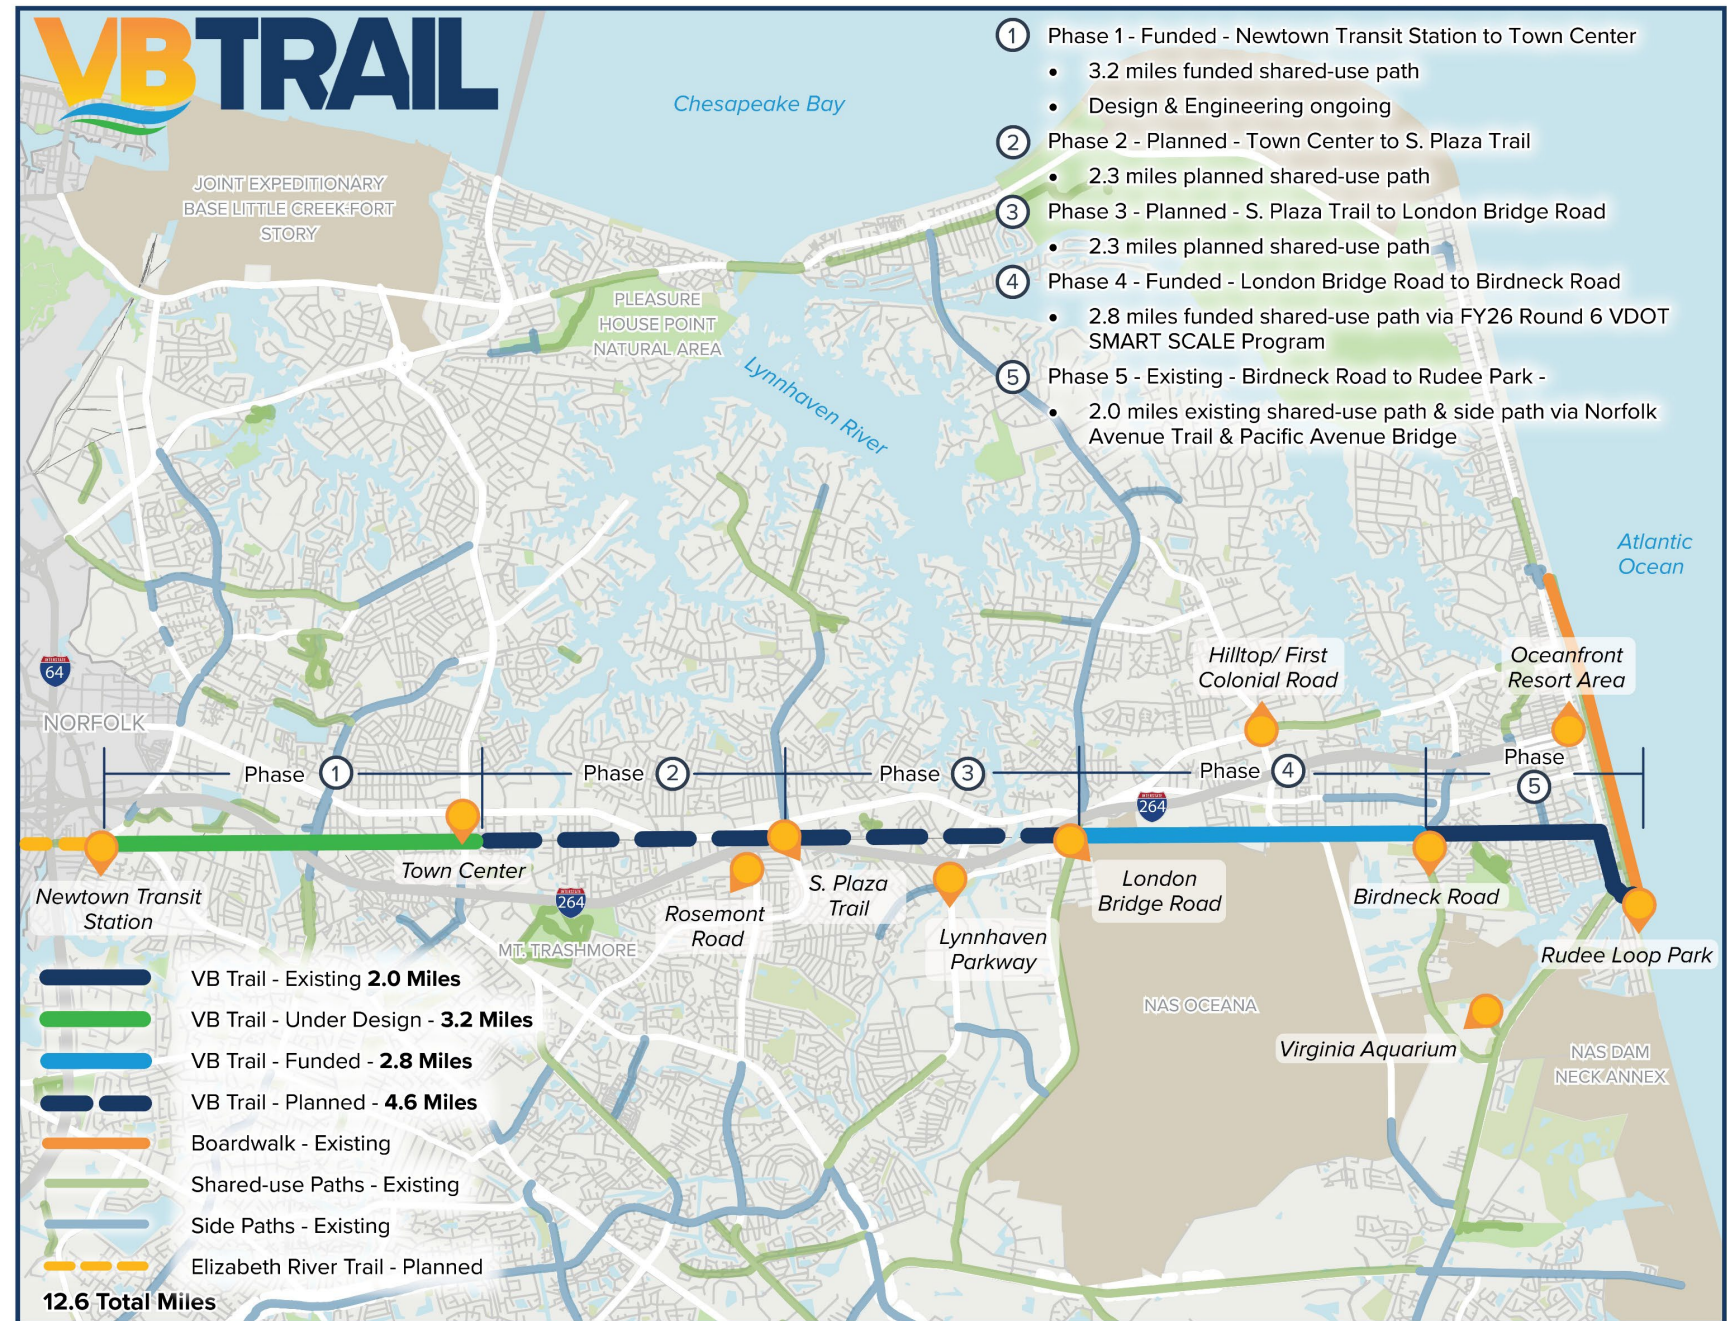

VB TRAIL Phase 1

Funding:


- 2022: **\$750k** HUD Grant (US Rep Luria)
- Nov 2023: **\$902k** from Dominion (offshore wind easement)
- Dec 2023: **\$14.9M** from USDOT's SS4A
- Jan 2024: **\$2.998M** City Council local match
- Apr 2024: **\$14.9M** from USDOT's RCN Grant

Status:

- 60% Design (Mid-June)
- Federal Agreement nearly complete
- 5-year completion horizon (once agreement in place)

Construction Cost Increases:

- Overall Cost: **\$19.6M → \$36M**
- FY 25-26 Budget: City Council approved **\$16.5M** in city funds

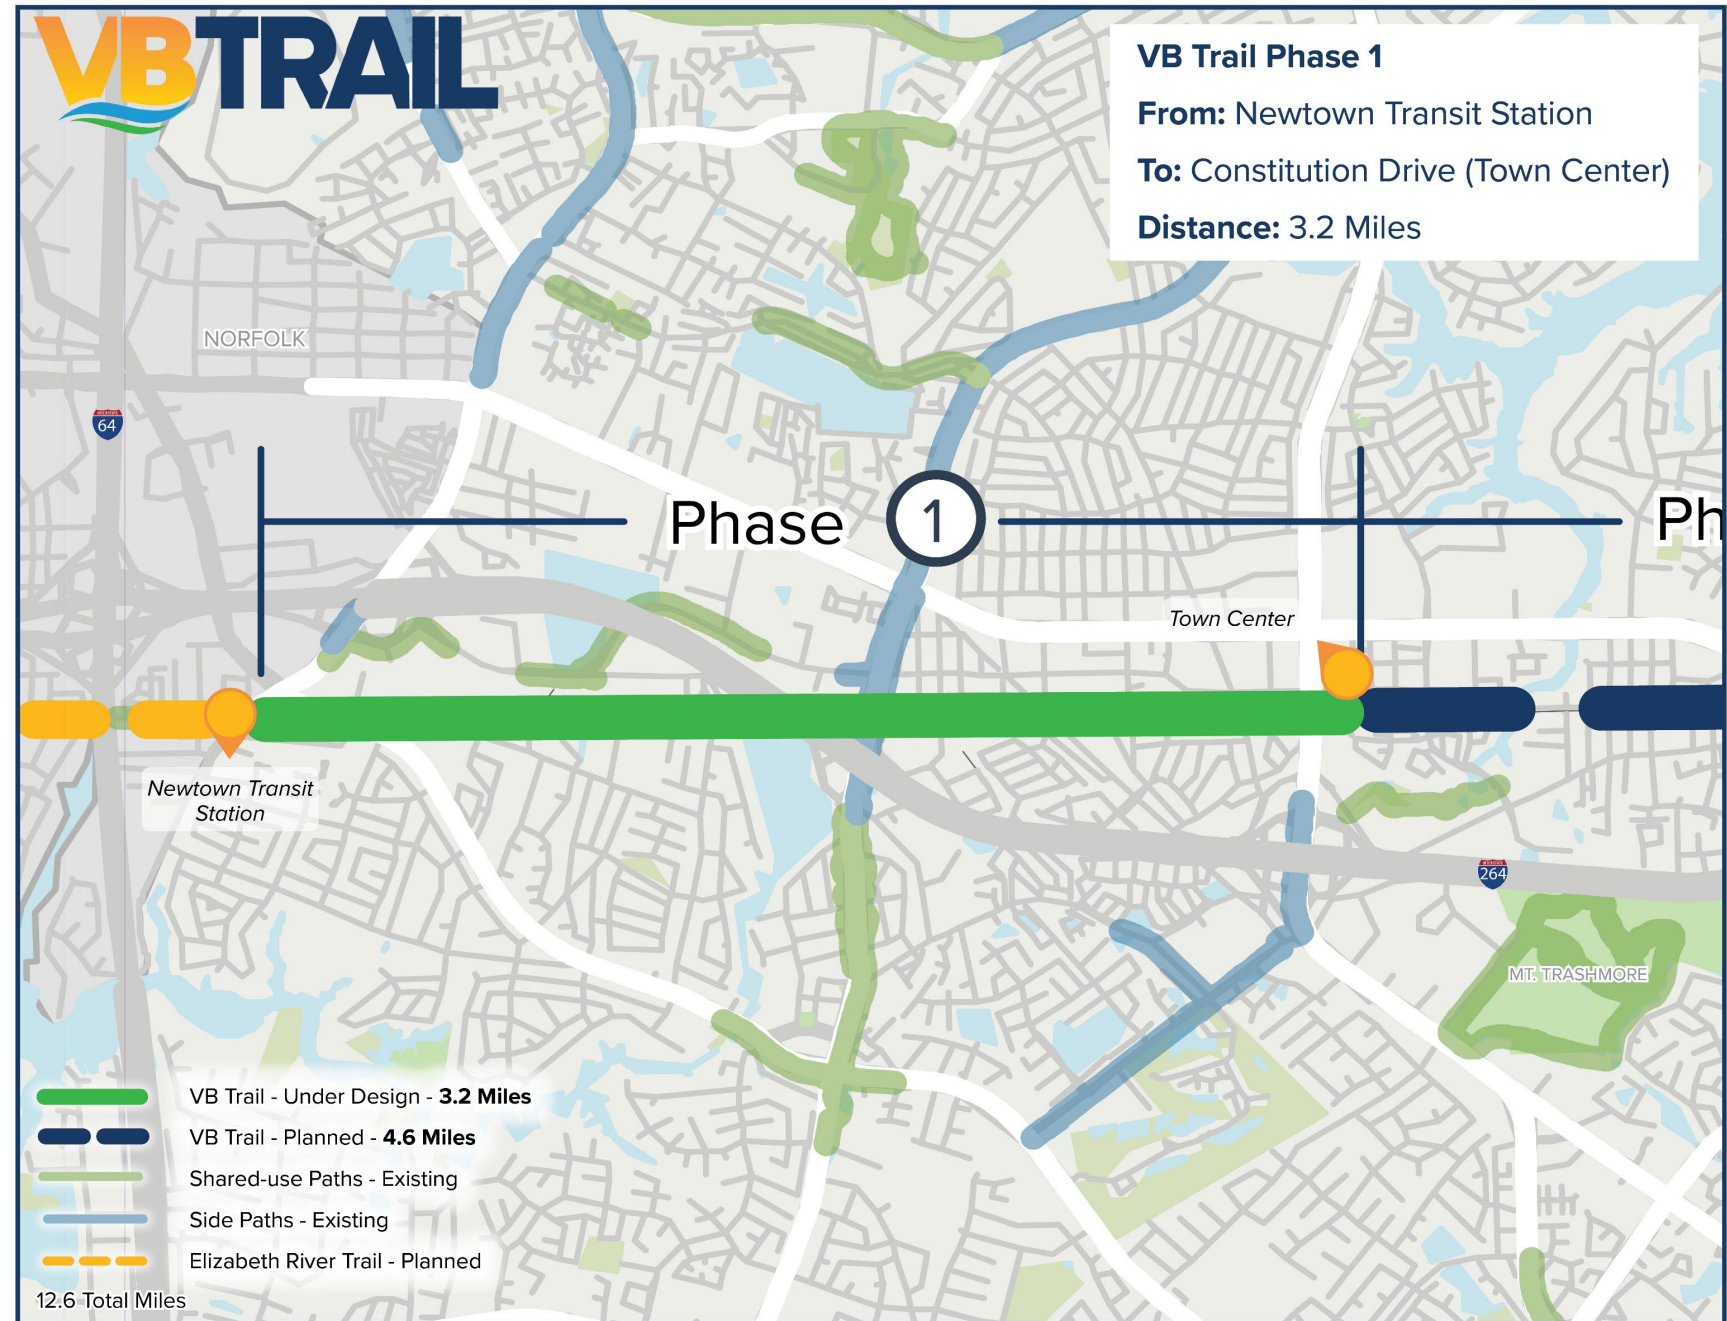

VB TRAIL Phase 1 - VB Trail Pedestrian Bridge Concept over Independence Boulevard



VB TRAIL Phase 2

Cost:


- \$45-50 Million

Status:

- Preliminary Engineering Report (15% Design) Complete
- Seeking Federal and State Grants

Key Improvements:

- **Intersections:** Rosemont Road, S. Plaza Trail
- **Crossings:** One Bridge over Thalia Creek
- **Connectivity:** Future Thalia Creek Greenway Phases

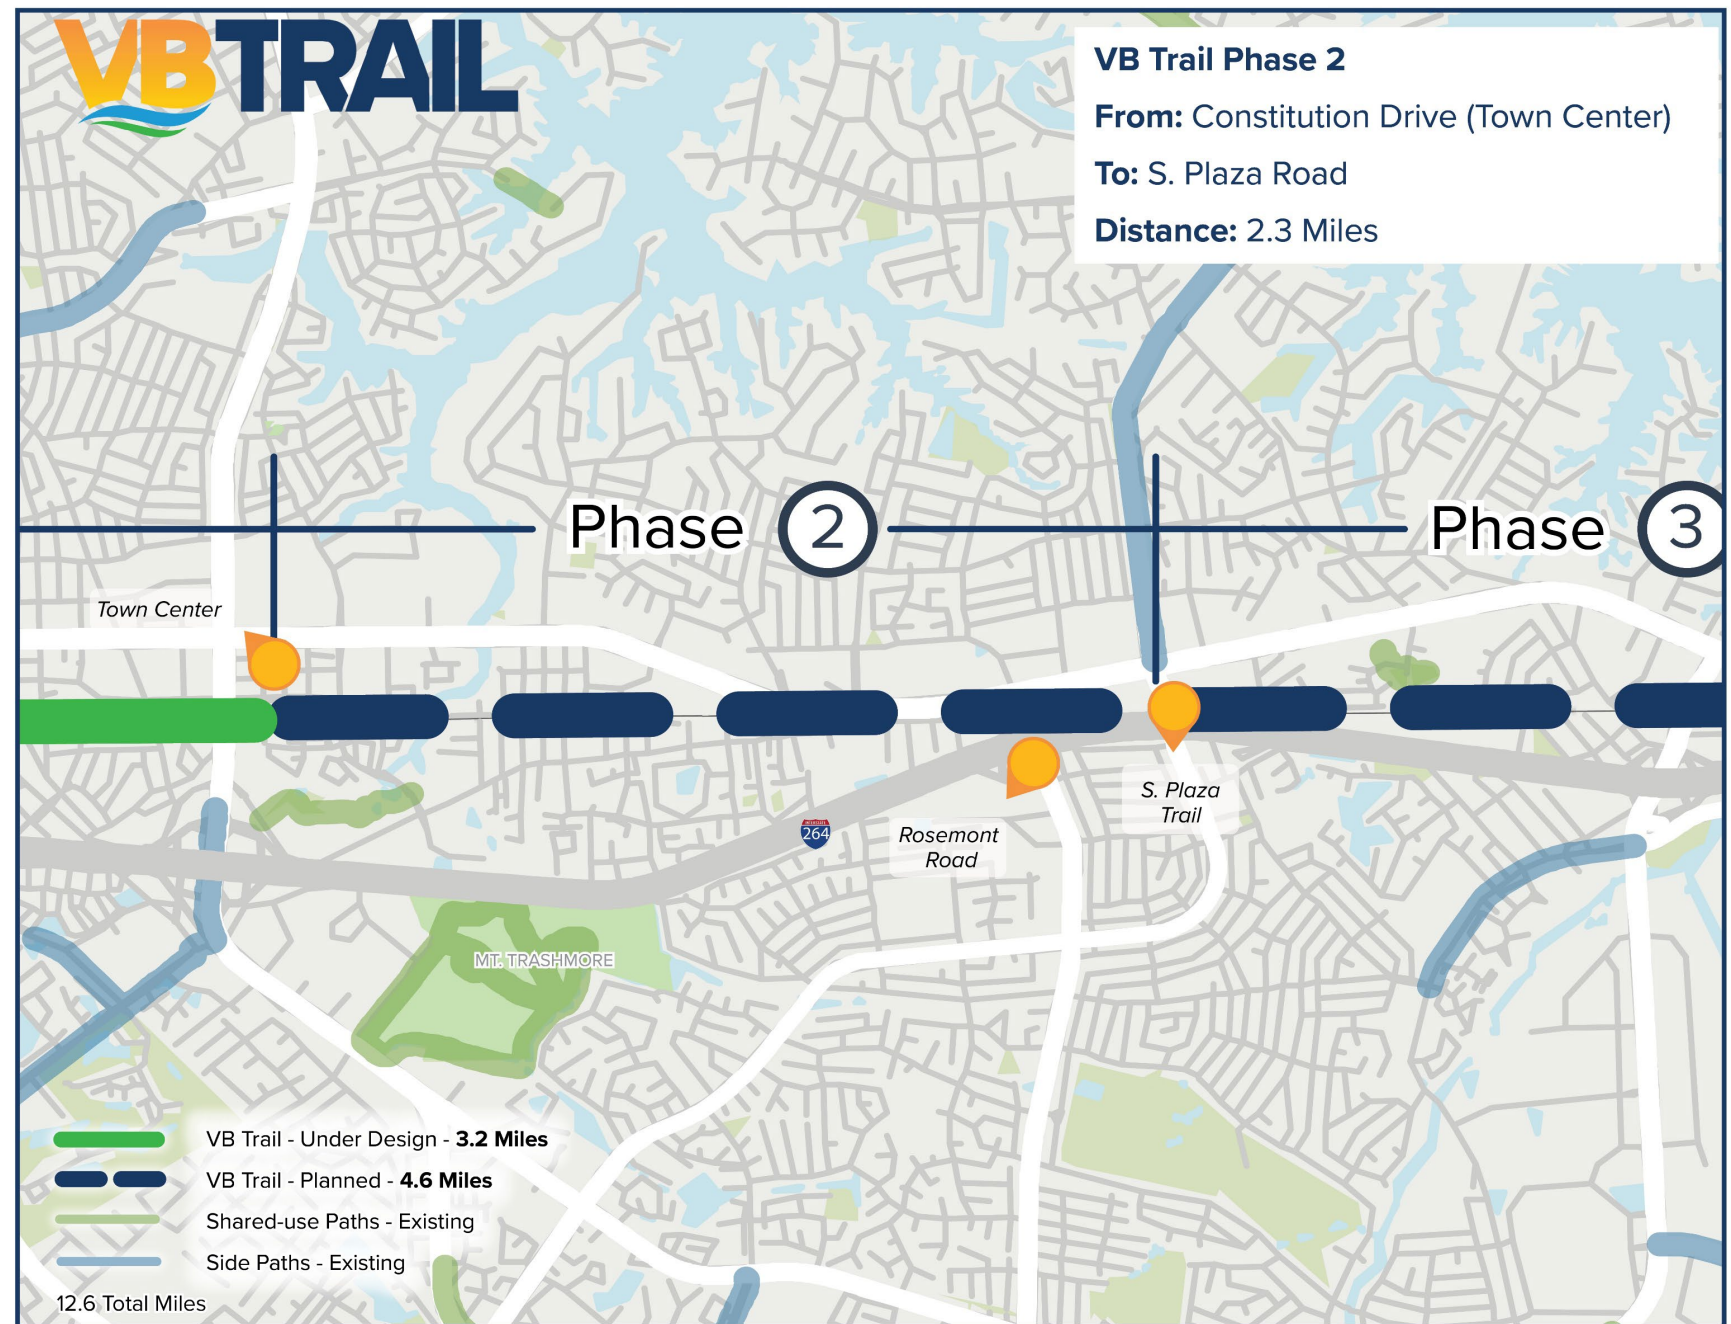

VB TRAIL Phase 3

Cost:


- \$25 - \$30 Million

Status:

- Seeking Federal and State Grants

Key Improvements:

- **Intersections:** Lynnhaven Road, London Bridge
- **Crossings:** One Bridge over London Bridge Creek
- **Connectivity:** Future Thalia Creek Greenway Phases

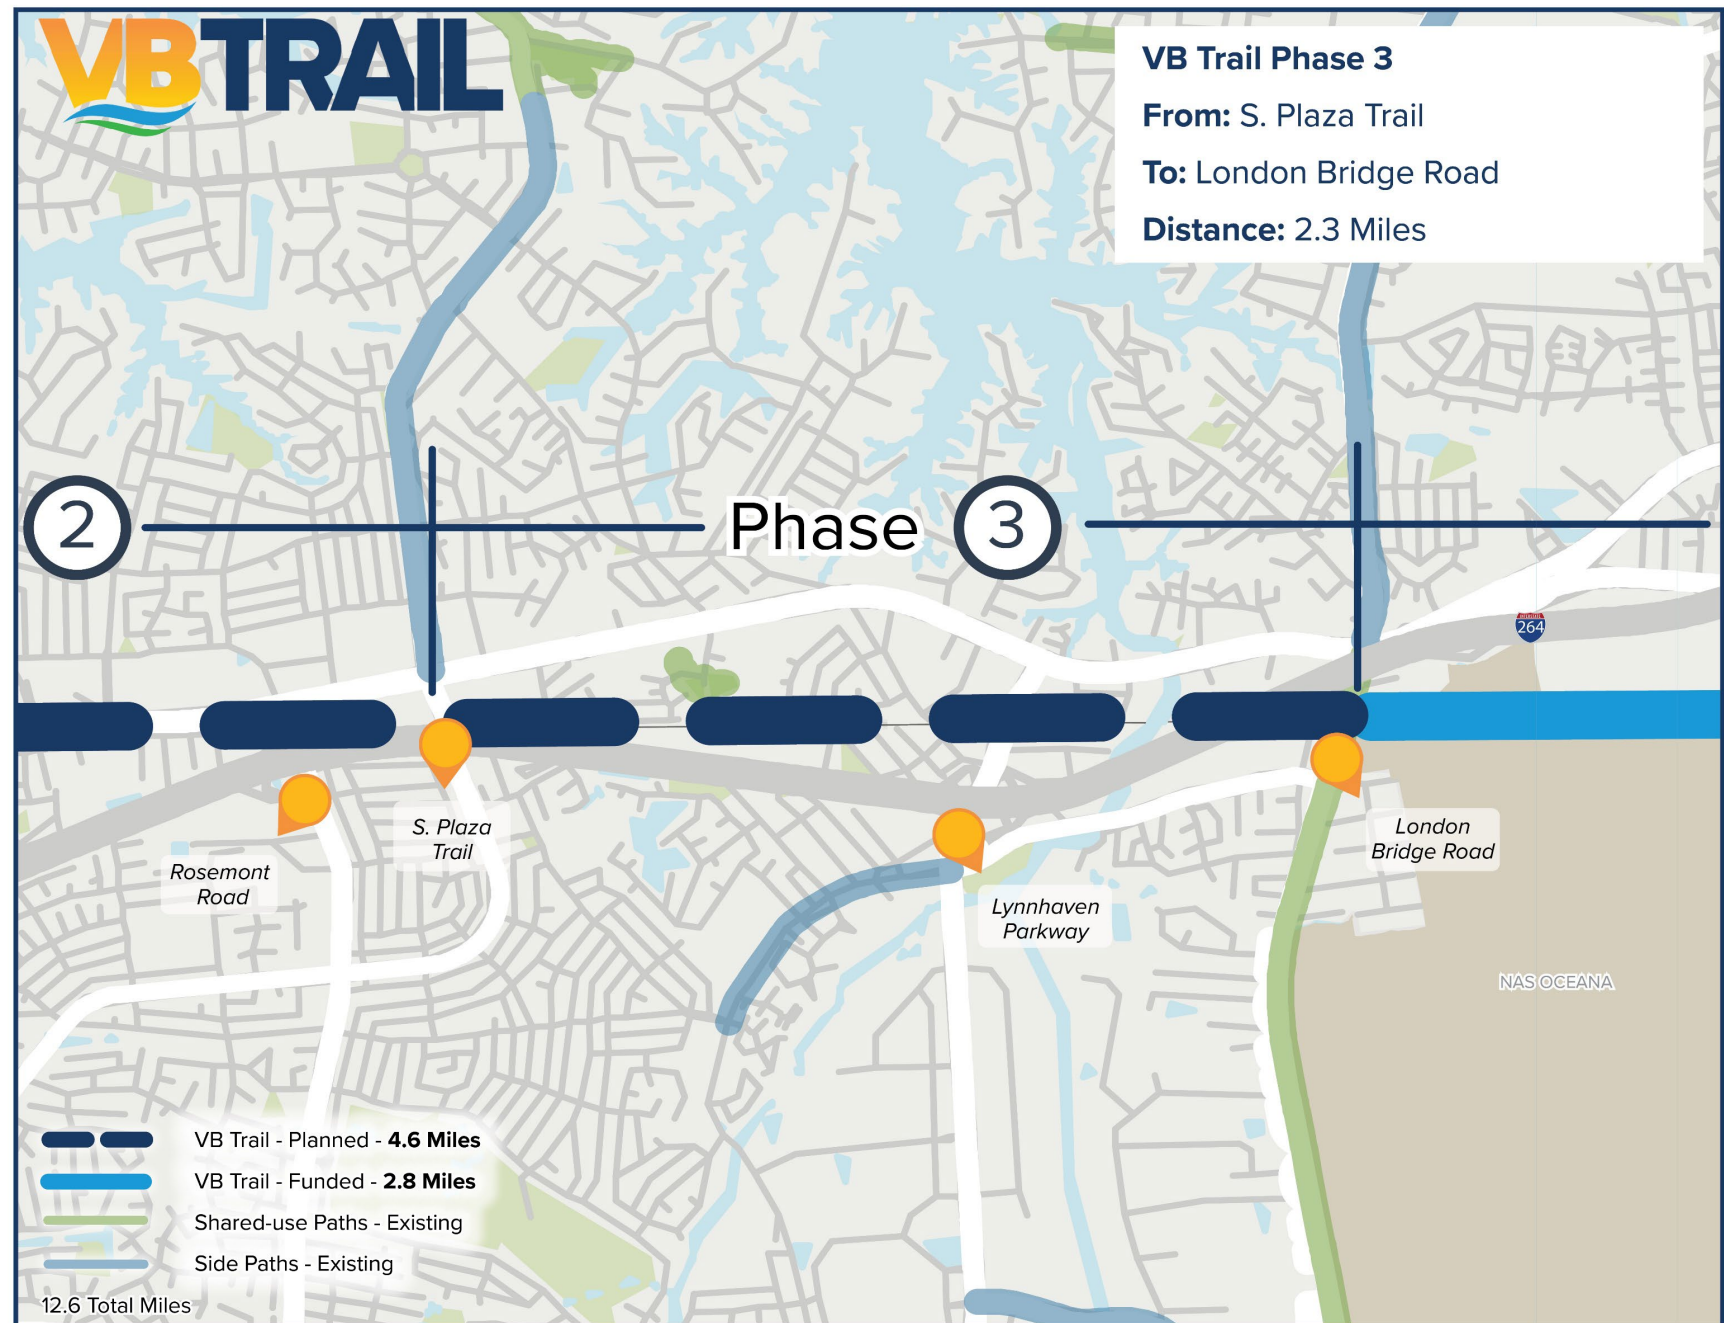


VB TRAIL Phase 4

Funding:

- June 2025 - **\$23.8 Million**
Round 6 SMART Scale Funding
- **Key Improvements:**
- **Intersections:** London Bridge Road, Oceana Boulevard, and S. Birdneck Road

Schedule:


- Design: 2027
- Construction: 2031-2032

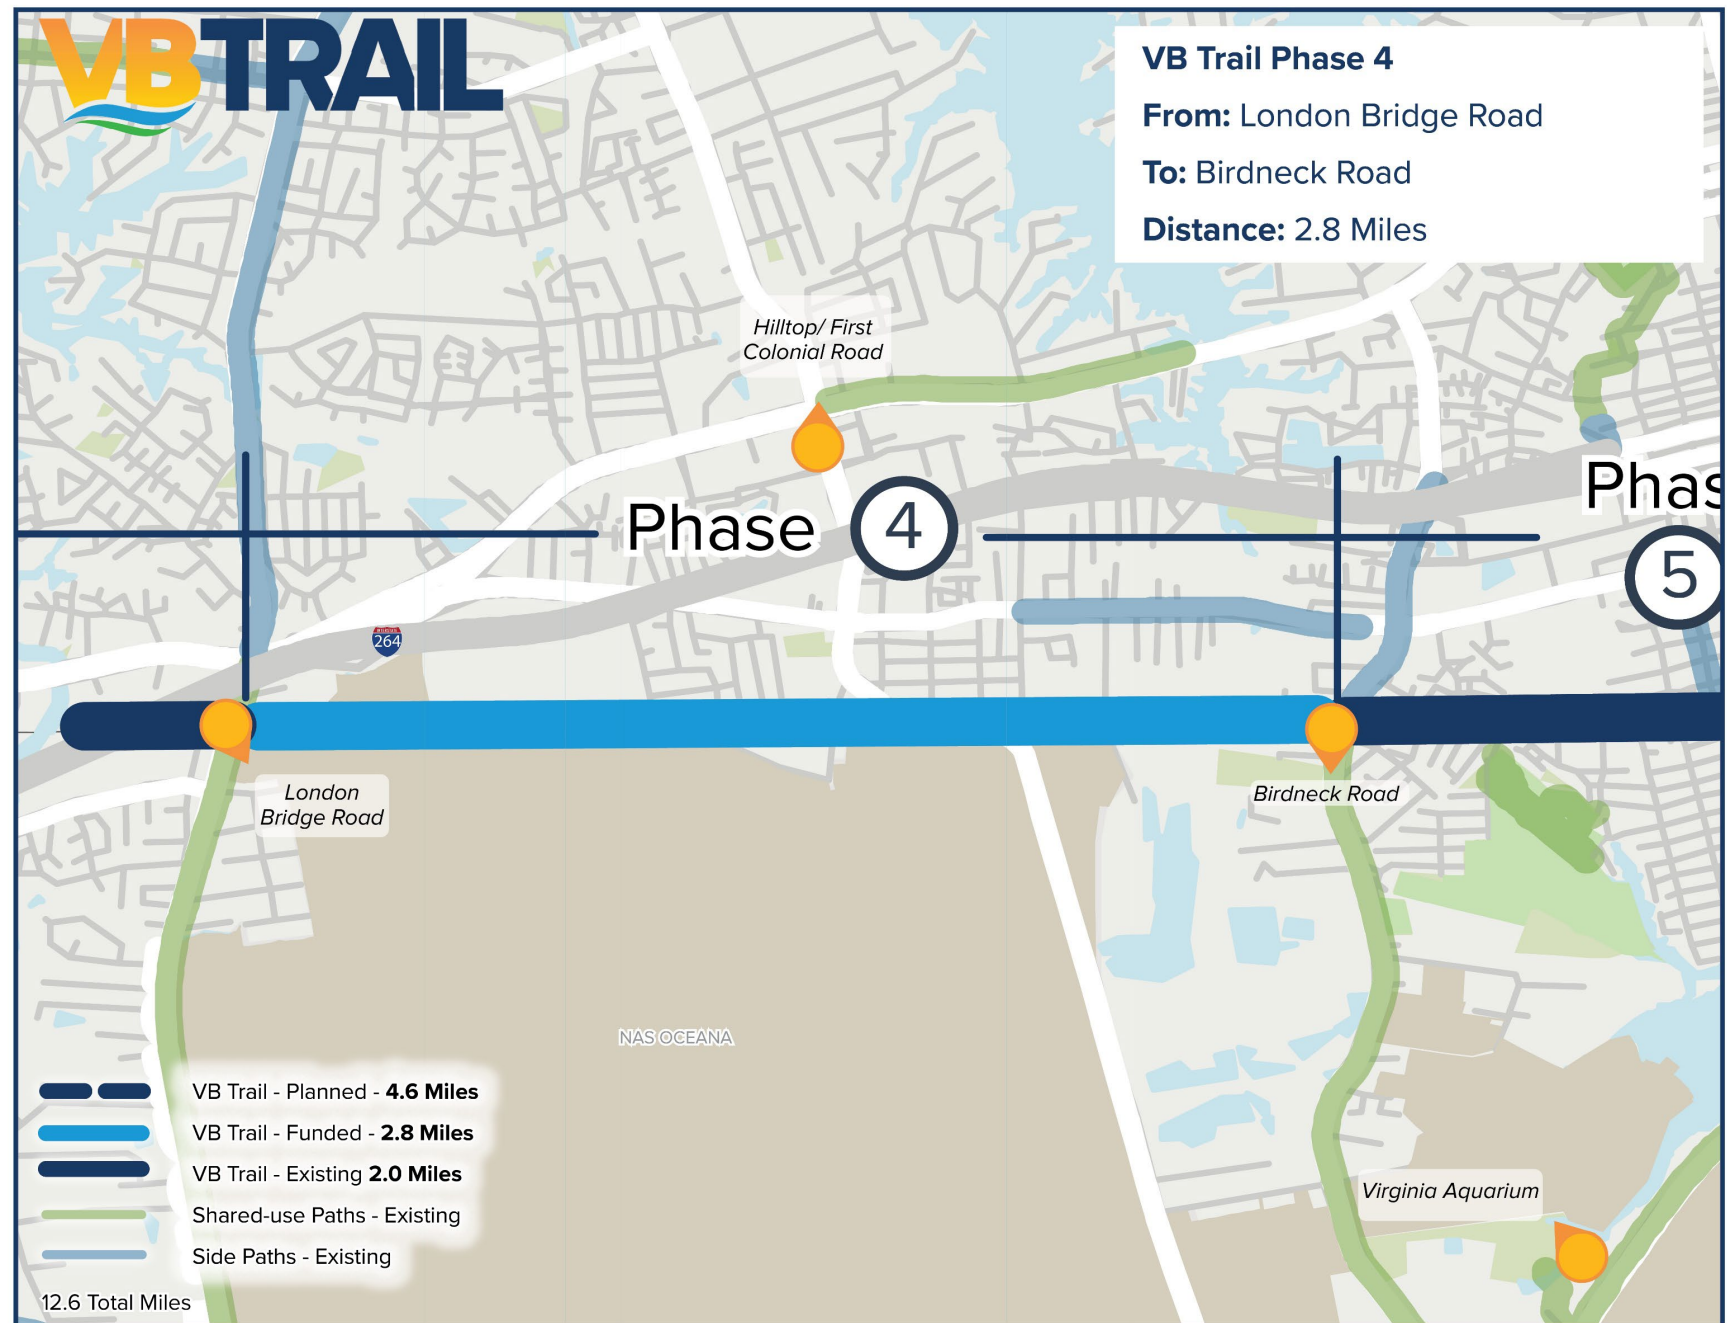

VB TRAIL Phase 5

Status:


- Norfolk Avenue Trail – Complete
- Pacific Avenue Boardwalk – Surface replaced – 2022 - **\$750K**
- Winston-Salem Avenue Improvements – Under Construction
- Rudee Park – Under Design

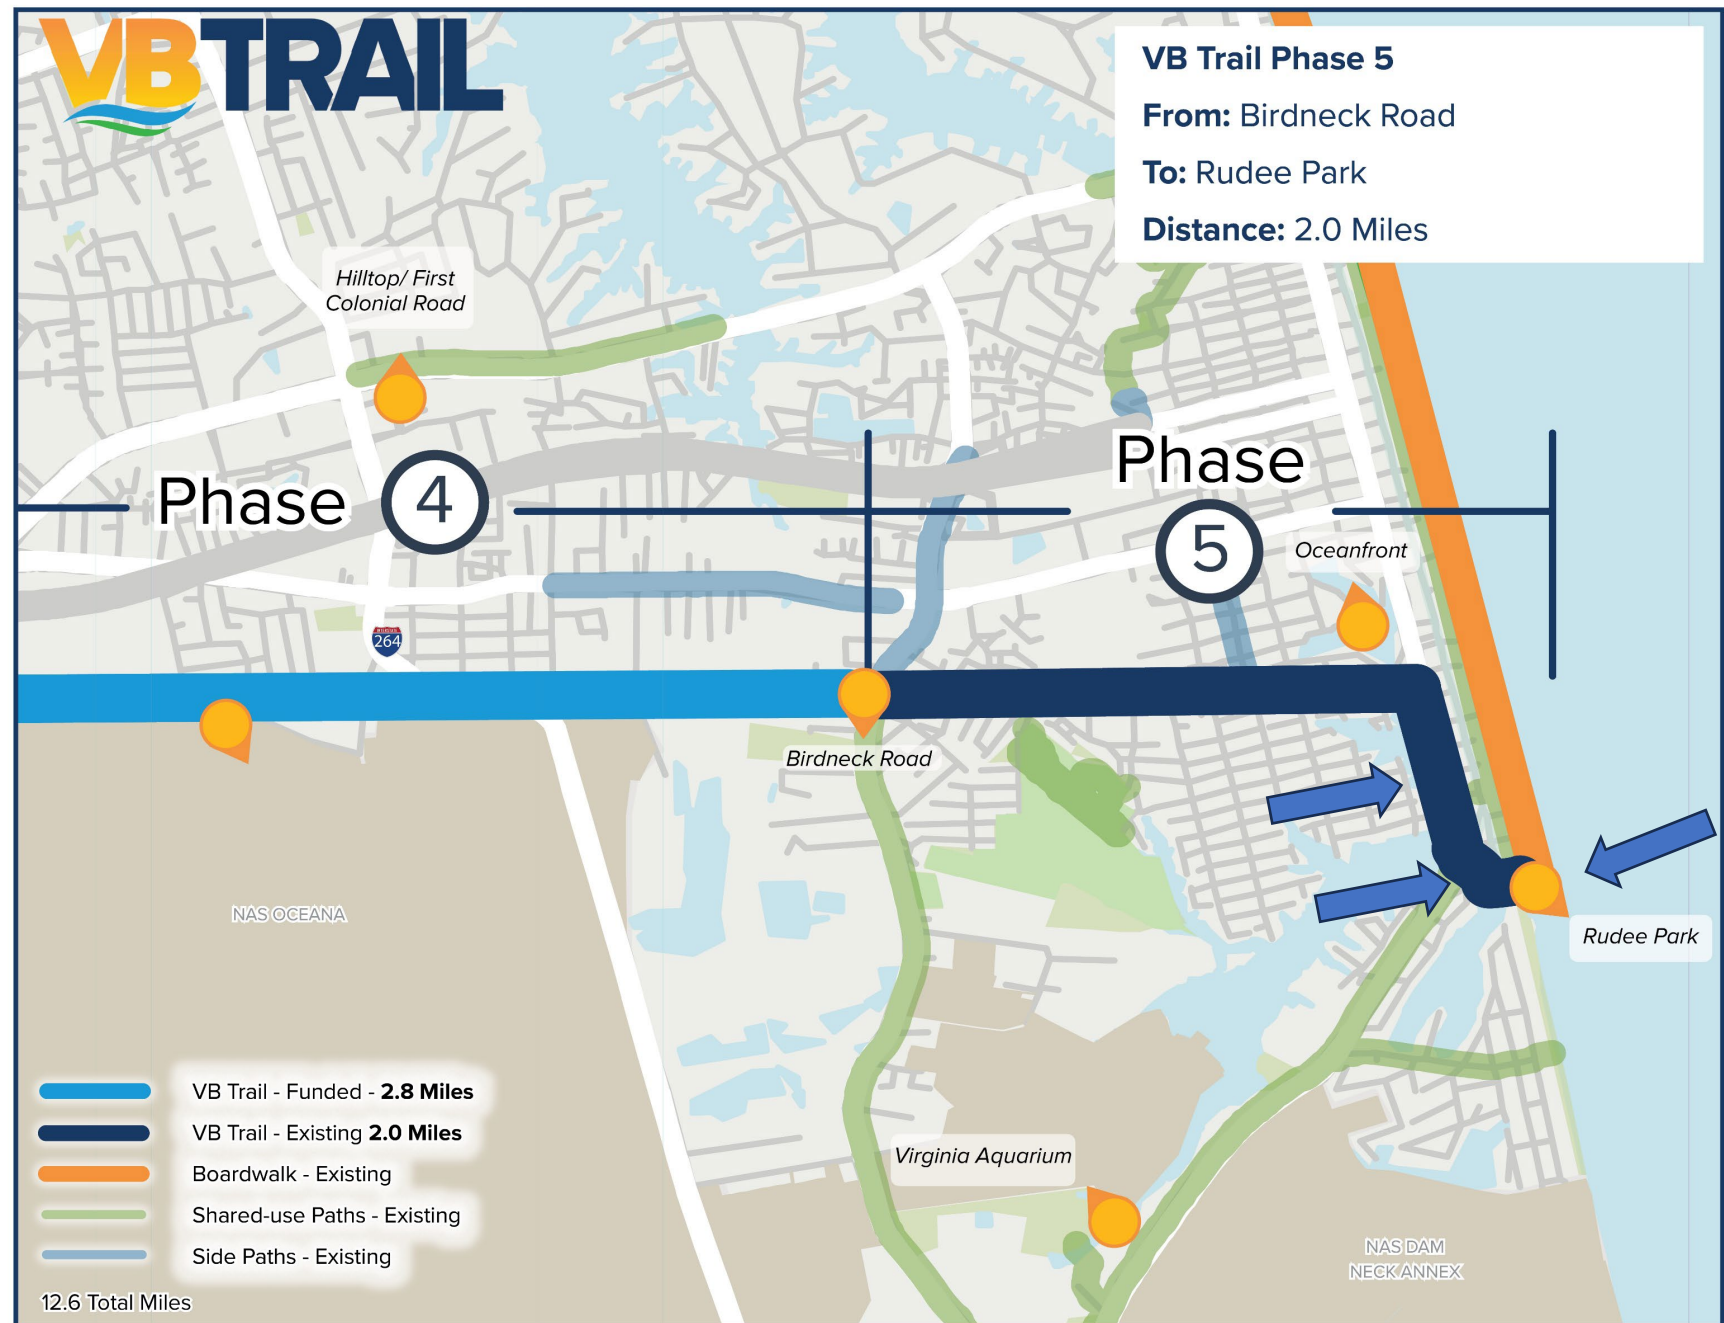



Phase 5 – Winston Salem Avenue Improvements

- \$18 Million City Investment
- Improving the Marina District to be more walkable and pedestrian friendly
- Last connection to the Eastern Terminus of the VB Trail, SHRT, Beaches to Bluegrass Trail, and TransAmerica Trail
- Improves stormwater and utilities along corridor
- Currently Under Construction

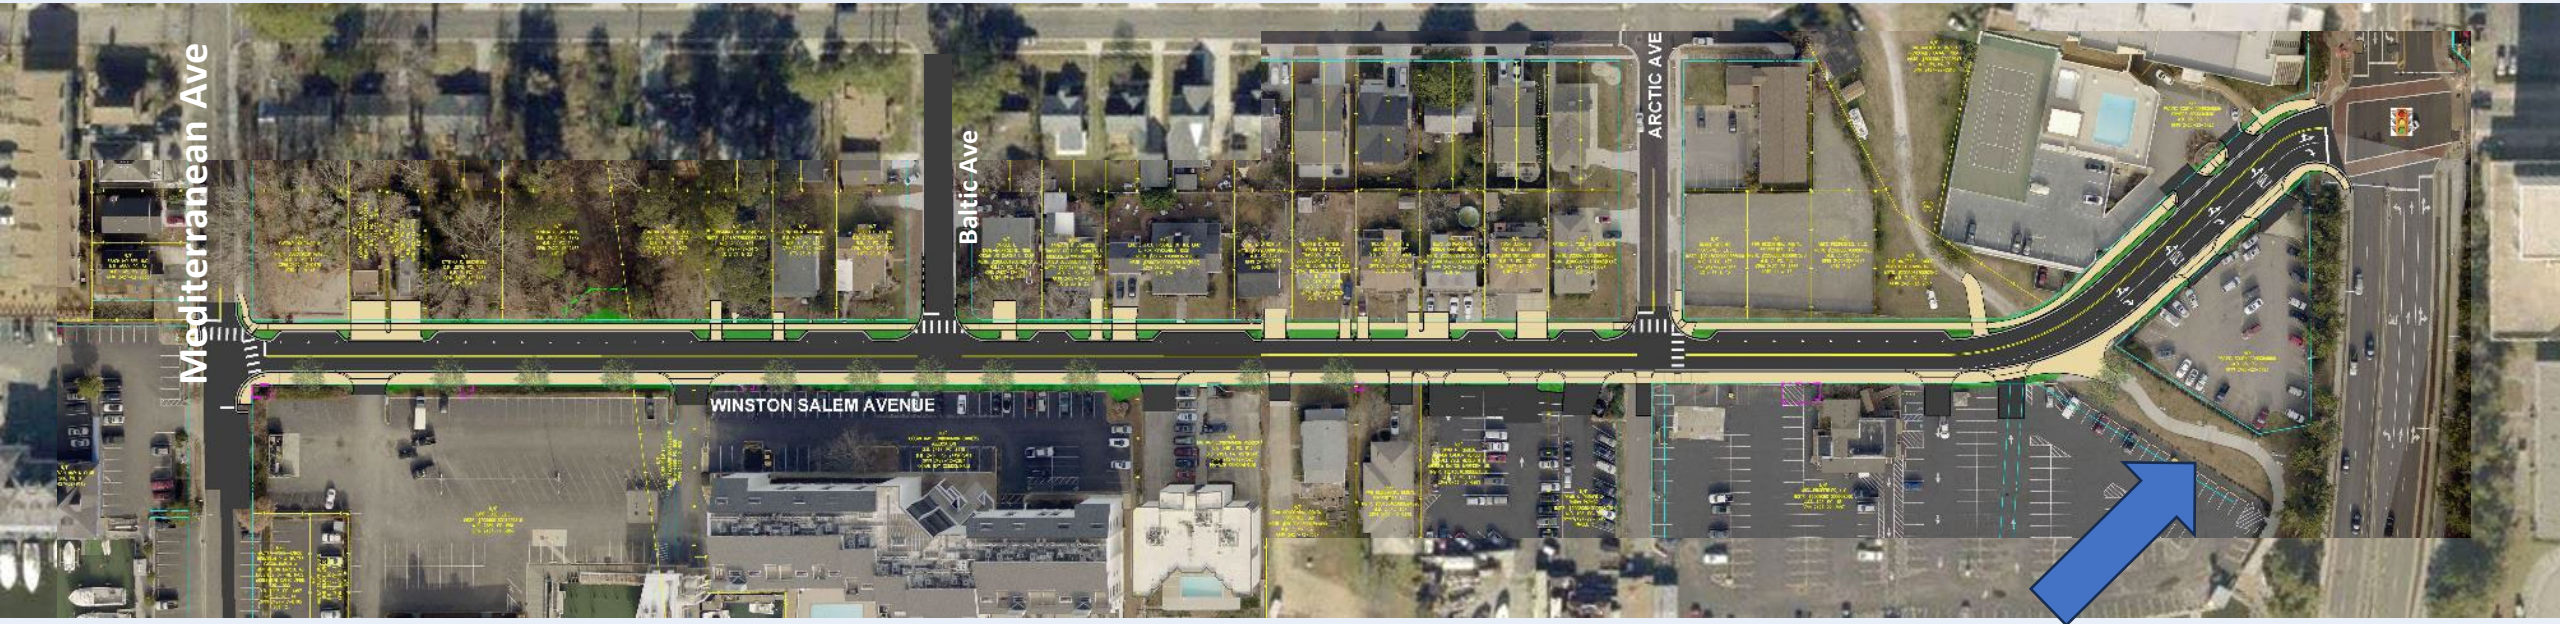

VBTRAIL Phase 5 – Winston Salem Avenue Improvements



Existing Conditions



Future Conditions

- \$42 Million City Investment
- The New Terminus of the VB Trail, SHRT, Beaches to Bluegrass Trail, and TransAmerica Trail ending in the **Atlantic Ocean** via the **Jetty Walk**
- Connects the VB Trail, Atlantic Avenue, and the Boardwalk
- Expected Construction: 2027 – 2028

VBTRAIL Phase 5 – Rudee Park



VBTRAIL Phase 5 – Rudee Park



VBTRAIL Phase 5 – Rudee Park



Thank you

Contact:

Steve Lambert

(757)385-4310

slambert@vbgov.com



**Parks &
Recreation**
